Town of New Glarus
Pioneer Road Reconstruction — Today: June 23, 2016
Project Schedule — Schedule Date: March 18, 2016
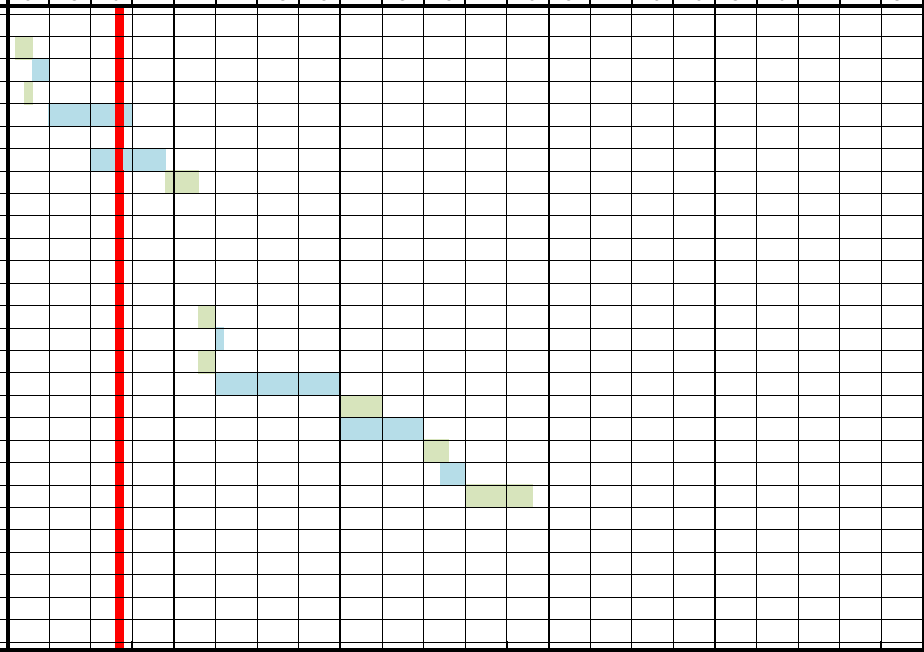
Phase	Description	Begin	End	Calendar Day
1	BEGIN PHASE I RECONSTRUCTION	June 7, 2016		-42528
1	Mobilization and Place Traffic Control	June 7, 2016	June 8, 2016	1
1	Place Erosion Control, Finish Grubbing	June 9, 2016	June 10, 2016	1
1	Pulverize Pavement	June 8, 2016	June 8, 2016	0
1	Grade Road Base	June 13, 2016	June 24, 2016	11
1	Extend Culverts, Place End Sections			
1	Install Base Course	June 20, 2016	June 30, 2016	10
1	Finish Grade and Pavement (Payne & Dolan)	July 1, 2016	July 6, 2016	5
1	Install Shoulders			
1	Restore Topsoil and Place Mulch & Matting			
1	END PHASE I RECONSTRUCTION			
2	BEGIN PHASE 2 RECONSTRUCTION			
2	Mobilization and Place Traffic Control	July 7, 2016	July 8, 2016	1
2	Place Erosion Control, Finish Grubbing	July 9, 2016	July 11, 2016	2
2	Pulverize Pavement	July 7, 2016	July 8, 2016	1
2	Grade Road Base	July 9, 2016	July 29, 2016	20
2	Extend Culverts, Place End Sections	August 1, 2016	August 5, 2016	4
2	Install Base Course	August 1, 2016	August 13, 2016	12
2	Finish Grade and Pavement (Payne & Dolan)	August 14, 2016	August 17, 2016	3
2	Install Shoulders	August 17, 2016	August 19, 2016	2
2	Restore Topsoil and Place Mulch & Matting	August 22, 2016	August 31, 2016	9
2	END PHASE 2 RECONSTRUCTION
